

Safety Advice 08-2012 (March)(NZ)

The following	Safety	Alert is	circulated	as an	EEA	Safety	Advice	courtesy	of
Transpower a	ind UGL	_ Infrastr	ucture.						

Scaffold Tube Failure


Date of event: 22 / 03 / 2012

Summary of Incident:

HSSE 19147 – High Potential Near Hit

A scaffold contractor was installing a piece of scaffold tube at the top of a section of scaffolding when the tube he was attached to (via safety harness and lanyard), broke as he leant back to step down.

As he started to fall backwards, he was grabbed by a co worker, preventing him from falling. The scaffolder was approximately 22 metres off the ground, as shown in photo below.

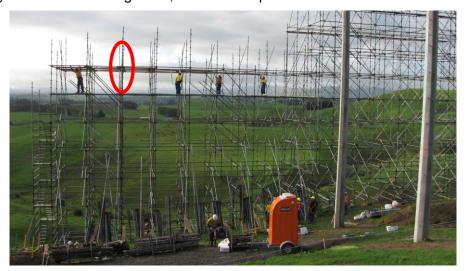

Scaffold depicting position of scaffolder at time of incident



Photo of the broken scaffold tube



© 2010 A UGL Limited Company ABN 96 096 365 972

Date: 14/10/2010



Initial Corrective Actions:

A Safety meeting held with all site personnel to discuss the seriousness of such an event.

All equipment was inspected to ensure no other defective equipment was on site, and a review was initiated of all erected scaffold to check for any defects that may have been previously missed.

The damaged tube is being inspected by engineers.

Review of inspection procedures before dispatching equipment to site is being undertaken.

Reminder to ensure the following:

All equipment must be thoroughly inspected before installing.

Operatives to ensure they are attached to a secure part of the structure at all times.

Refer to the publication "Best Practice Guidelines for Scaffolding in New Zealand" for scaffolding requirements.

A full incident investigation is under way.

Authorised by: (please print name and position title)				
Alliance HSSQ Manager	Steven Notman			
Alliance Manager	Ian Ditchfield			



Date: 14/10/2010

Project Name:

This is to verify that this Safety Alert has been received and the		Tick		
following steps taken to <u>IDENTIFY</u> and <u>REDUCE THE RISK</u> of a similar occurrence on this site/project:	Yes	No		
1. Is this incident relevant to your site/project? Is there a risk of a				
similar incident or similar circumstances occurring?				
If the answer is NO, then sign bottom of the sheet and forward copy to relevant site				
HSSE representative.				
If the answer is YES, complete questions 2-4 before signing and forwarding a copy				
to the relevant site HSSE representative.				
2. Have the contents of the Safety Alert been Toolboxed with				
employees and subcontractors?				
3. Has a copy of the Safety Alert been placed on notice boards?				
4. Has the site/project HIDRA been updated?				

Comments:

Verified by (please print name)	Signed	Date
<hsse representative=""></hsse>		

(Once completed a copy of this notification sheet is to be forwarded to the relevant site HSSE representative and the original must be filed on site along with all documentation supporting the action that was taken (this may be required for future auditing purposes).



© 2010 A UGL Limited Company ABN 96 096 365 972

Date: 14/10/2010
