TRANSPOWER

FIRST ALERT

Date: 18 July 2014

Haywards - Live control cable, arc-over

EVENT

Date of incident: Thursday 10th July 2014

During the re wiring of a marshalling cabinet, an arc-over occurred when cable cores were being fed through a cable gland. The cable was considered to be isolated prior to the work being carried out.

Cable cores were found to be 'live'. *They were not tested before work was started.*

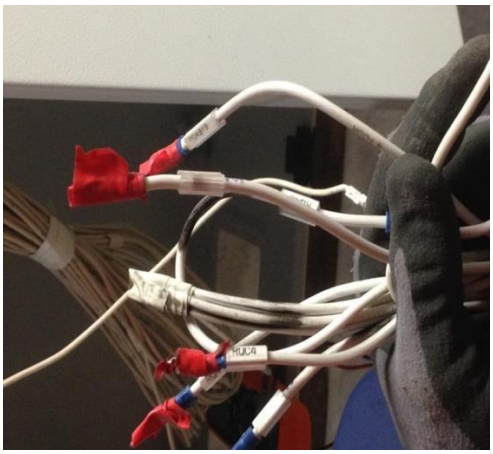

IMMEDIATE ACTIONS

- Work stopped while an investigation is being carried out
- Cable isolations rechecked and made safe

safeT WORK SAFE

For more information please contact:

Name Neill Kinniburgh
Designation Project Manager
Mob: 021 634555
neill.kinniburgh@transpower.co.nz
